


Activity ID	Activity Name	Orig Dur	Start	Finish	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	9
College of Marin																	
Indian Valley Campus																	
I21 - Organic Farm/Garden Enhancements																	
	Design				[Gantt bar: 2017-2018]												
	DSA				[Gantt bar: 2017-2018]												
	Procurement				[Gantt bar: 2017-2018]												
	Construction				[Gantt bar: 2017-2018]												
	Closeout				[Gantt bar: 2017-2018]												
I22 - Maintenance & Operations Building																	
A9330	Consolidated to K07 Maintenance & Operations Building via BLR#1	0		11-May-17 A	◆ Consolidated to K07 Maintenance & Operations Building via BLR#1												
I23 - Storage																	
A9320	Consolidated to K07 Maintenance & Operations Building via BLR#1	0		11-May-17 A	◆ Consolidated to K07 Maintenance & Operations Building via BLR#1												
I24 - New Aquatics Center																	
A9340	Consolidated to I51 Miwok Cluster via BLR#1	0		11-May-17 A	◆ Consolidated to I51 Miwok Cluster via BLR#1												
I25 - ADA Barrier Removal/Site Improvements																	
	Design				[Gantt bar: 2018-2019]												
	DSA				[Gantt bar: 2018-2019]												
	Procurement				[Gantt bar: 2018-2019]												
	Construction				[Gantt bar: 2018-2019]												
	Closeout				[Gantt bar: 2018-2019]												
I26 - Jonas Center and Building 18																	
	Bridging Documents				[Gantt bar: 2017-2018]												
	Procurement				[Gantt bar: 2017-2018]												
	Design				[Gantt bar: 2017-2018]												
	DSA				[Gantt bar: 2017-2018]												
	Construction				[Gantt bar: 2017-2018]												
	Closeout				[Gantt bar: 2017-2018]												
	Building 18 Roof				[Gantt bar: 2017-2018]												
I47 - Building 27 (Dental, EMT, Court Reporting, Library)																	
	Design				[Gantt bar: 2018-2019]												
	DSA				[Gantt bar: 2018-2019]												
	Procurement				[Gantt bar: 2018-2019]												
	Construction				[Gantt bar: 2018-2019]												
	Closeout				[Gantt bar: 2018-2019]												
I49 - Pomo Cluster (Buildings 1-7)																	
	Exterior Envelope - Phase I				[Gantt bar: 2017-2018]												
	Interior Renovation - Phase II				[Gantt bar: 2017-2018]												
I50 - Admin Cluster (Buildings 8-12)																	
	Building 11				[Gantt bar: 2017-2018]												
	Generator				[Gantt bar: 2017-2018]												
	Buildings 8 & 9				[Gantt bar: 2017-2018]												
	Roofs 8,9,10,12, and 18				[Gantt bar: 2017-2018]												
	Windows 5, 9, and 12 (Split Funded Bldg 5 from I49)				[Gantt bar: 2017-2018]												
I51 - Miwok Cluster (Buildings 13-17)																	
	Procurement				[Gantt bar: 2017-2018]												
	Design				[Gantt bar: 2017-2018]												
	DSA				[Gantt bar: 2017-2018]												
	Construction				[Gantt bar: 2017-2018]												
	Closeout				[Gantt bar: 2017-2018]												
I52 - IVC Tree Study and Removal Project																	
A9350	Project Cancelled via BLR#1	0		11-May-17 A	◆ Project Cancelled via BLR#1												

Finish Date: 01-Aug-28
 Data Date: 01-Jan-17
 Run Date: 11-Jul-17 11:05
 Page 1 of 5
 COM-001

■ Remaining Level of Effort ◆ Critical Milestones
■ Actual Level of Effort ◆ Milestone
■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Summary Milestones

College of Marin



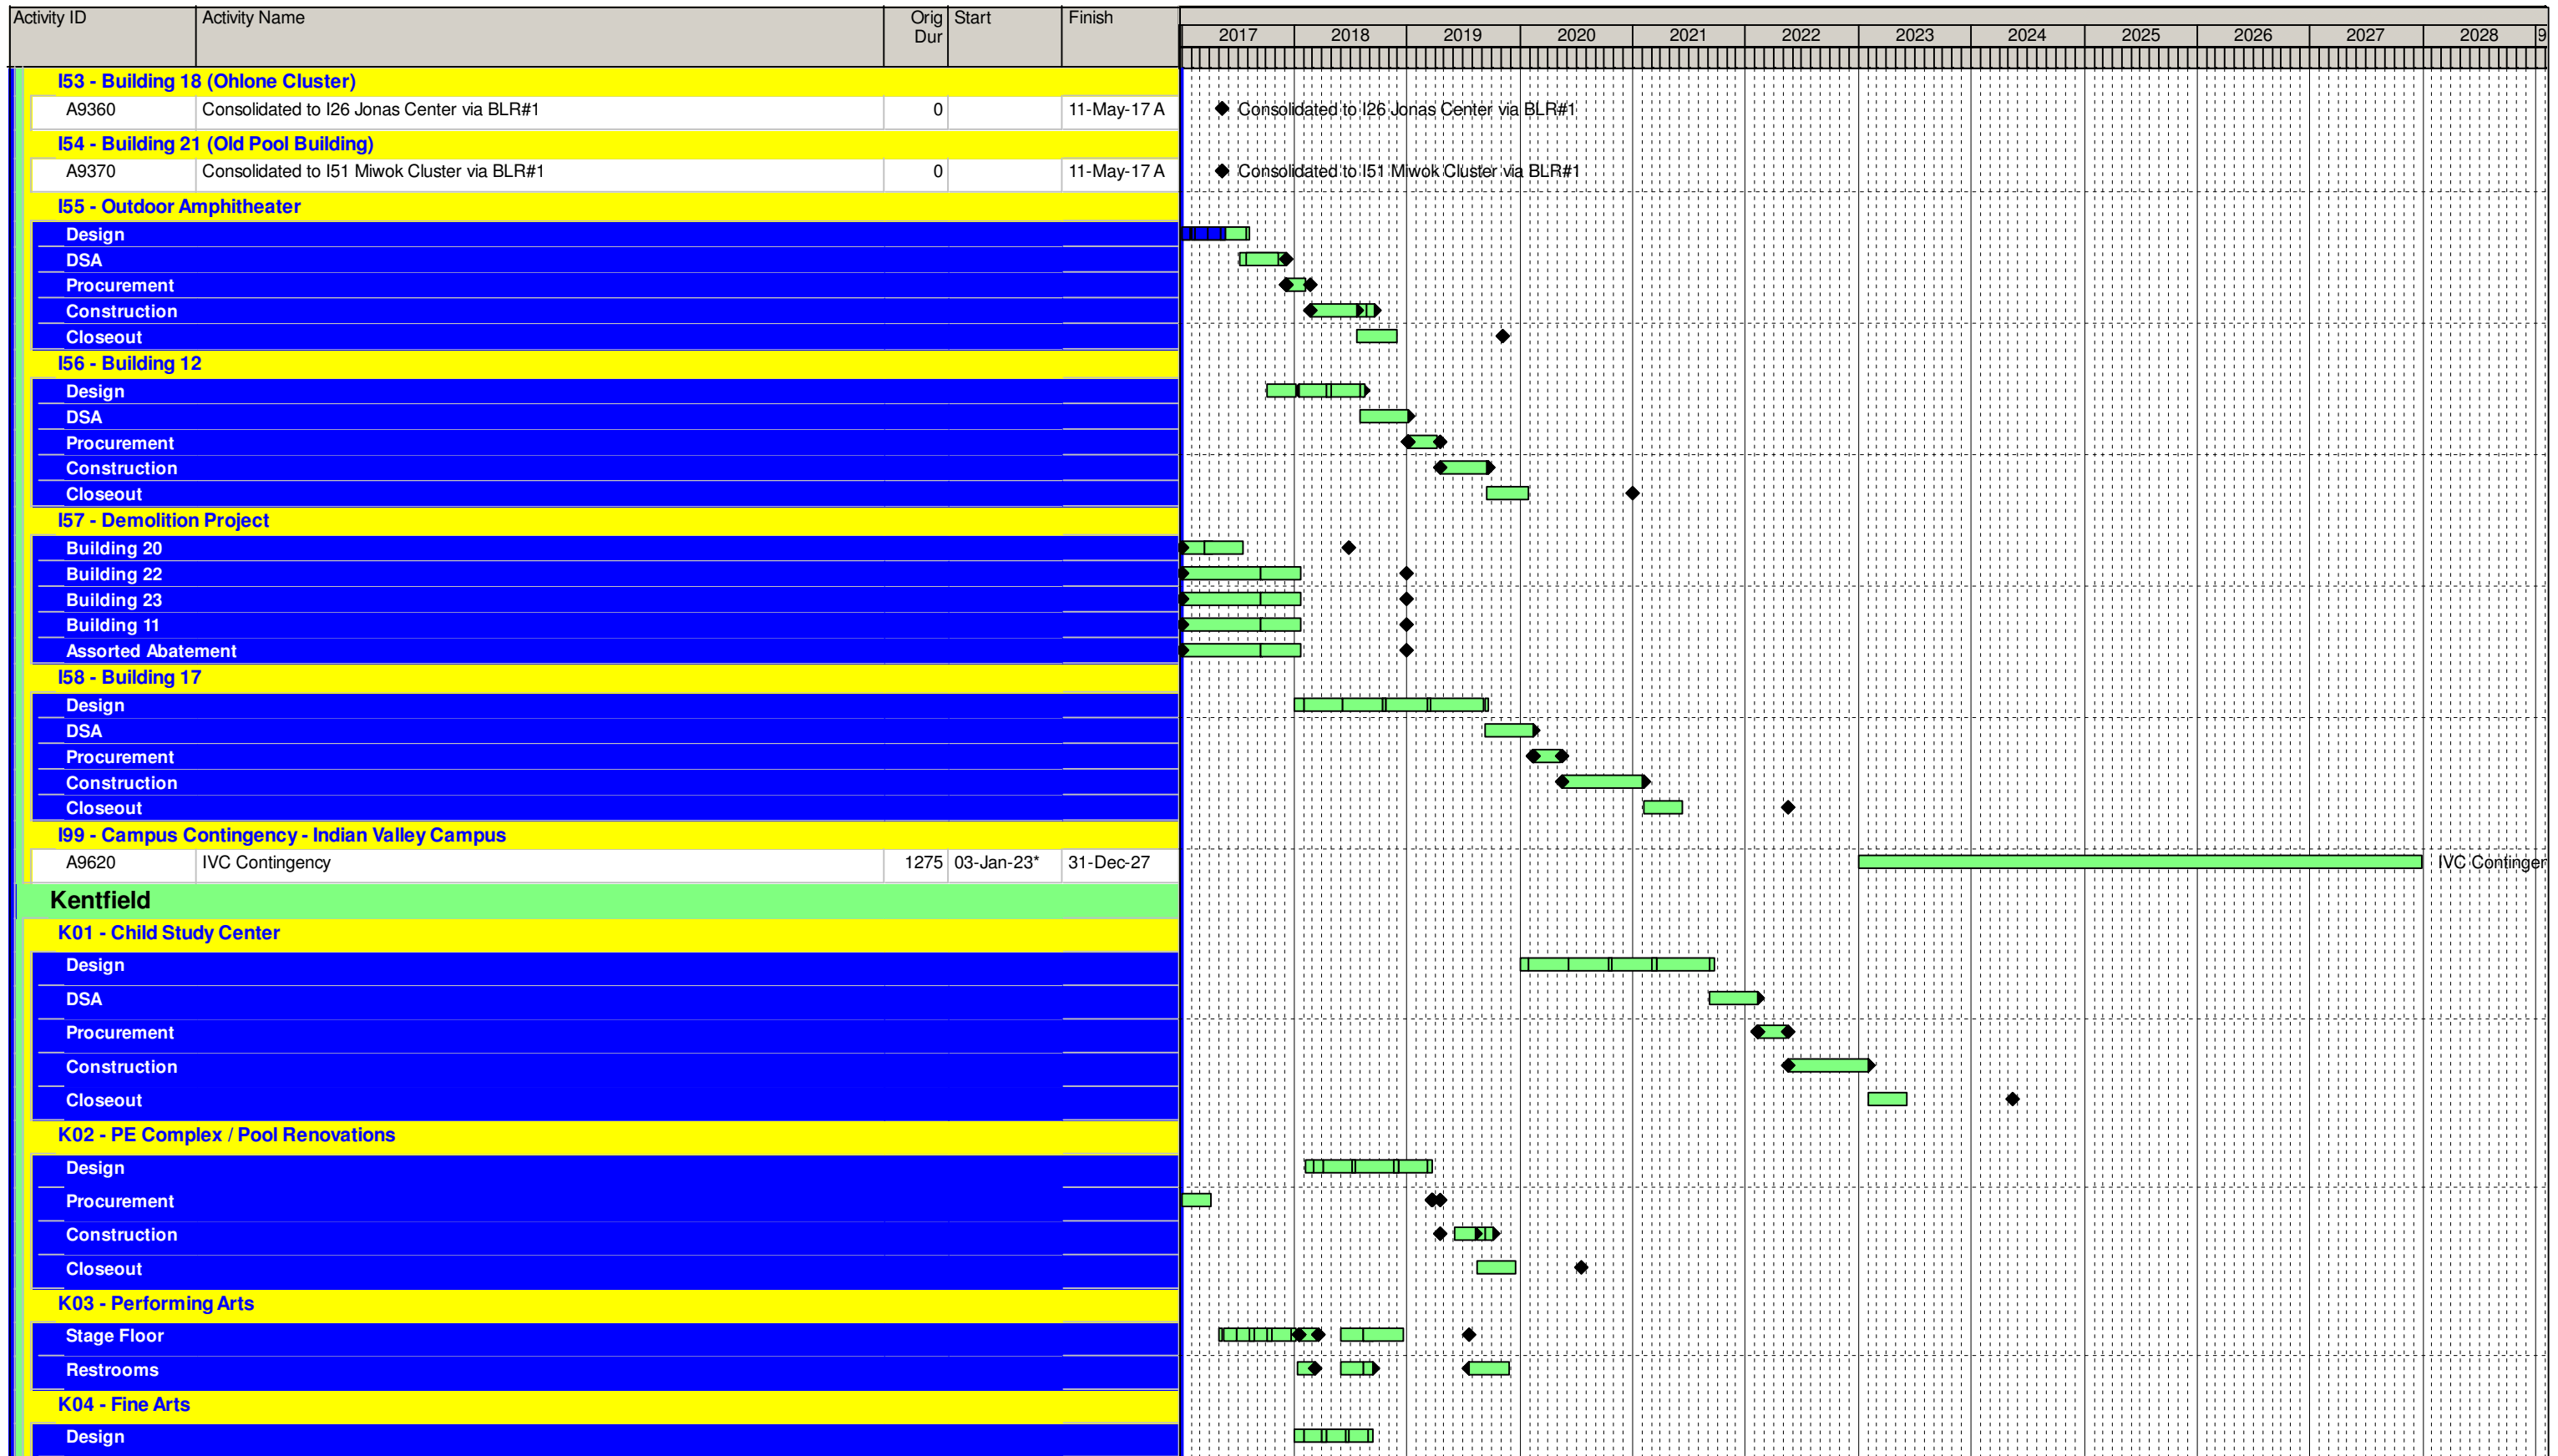


Finish Date: 01-Aug-28
 Data Date: 01-Jan-17
 Run Date: 11-Jul-17 11:05
 Page 2 of 5
 COM-001


	Remaining Level of Effort		Critical Milestones
	Actual Level of Effort		Milestone
	Actual Work		
	Remaining Work		
	Critical Remaining Work		
	Summary Milestones		

College of Marin



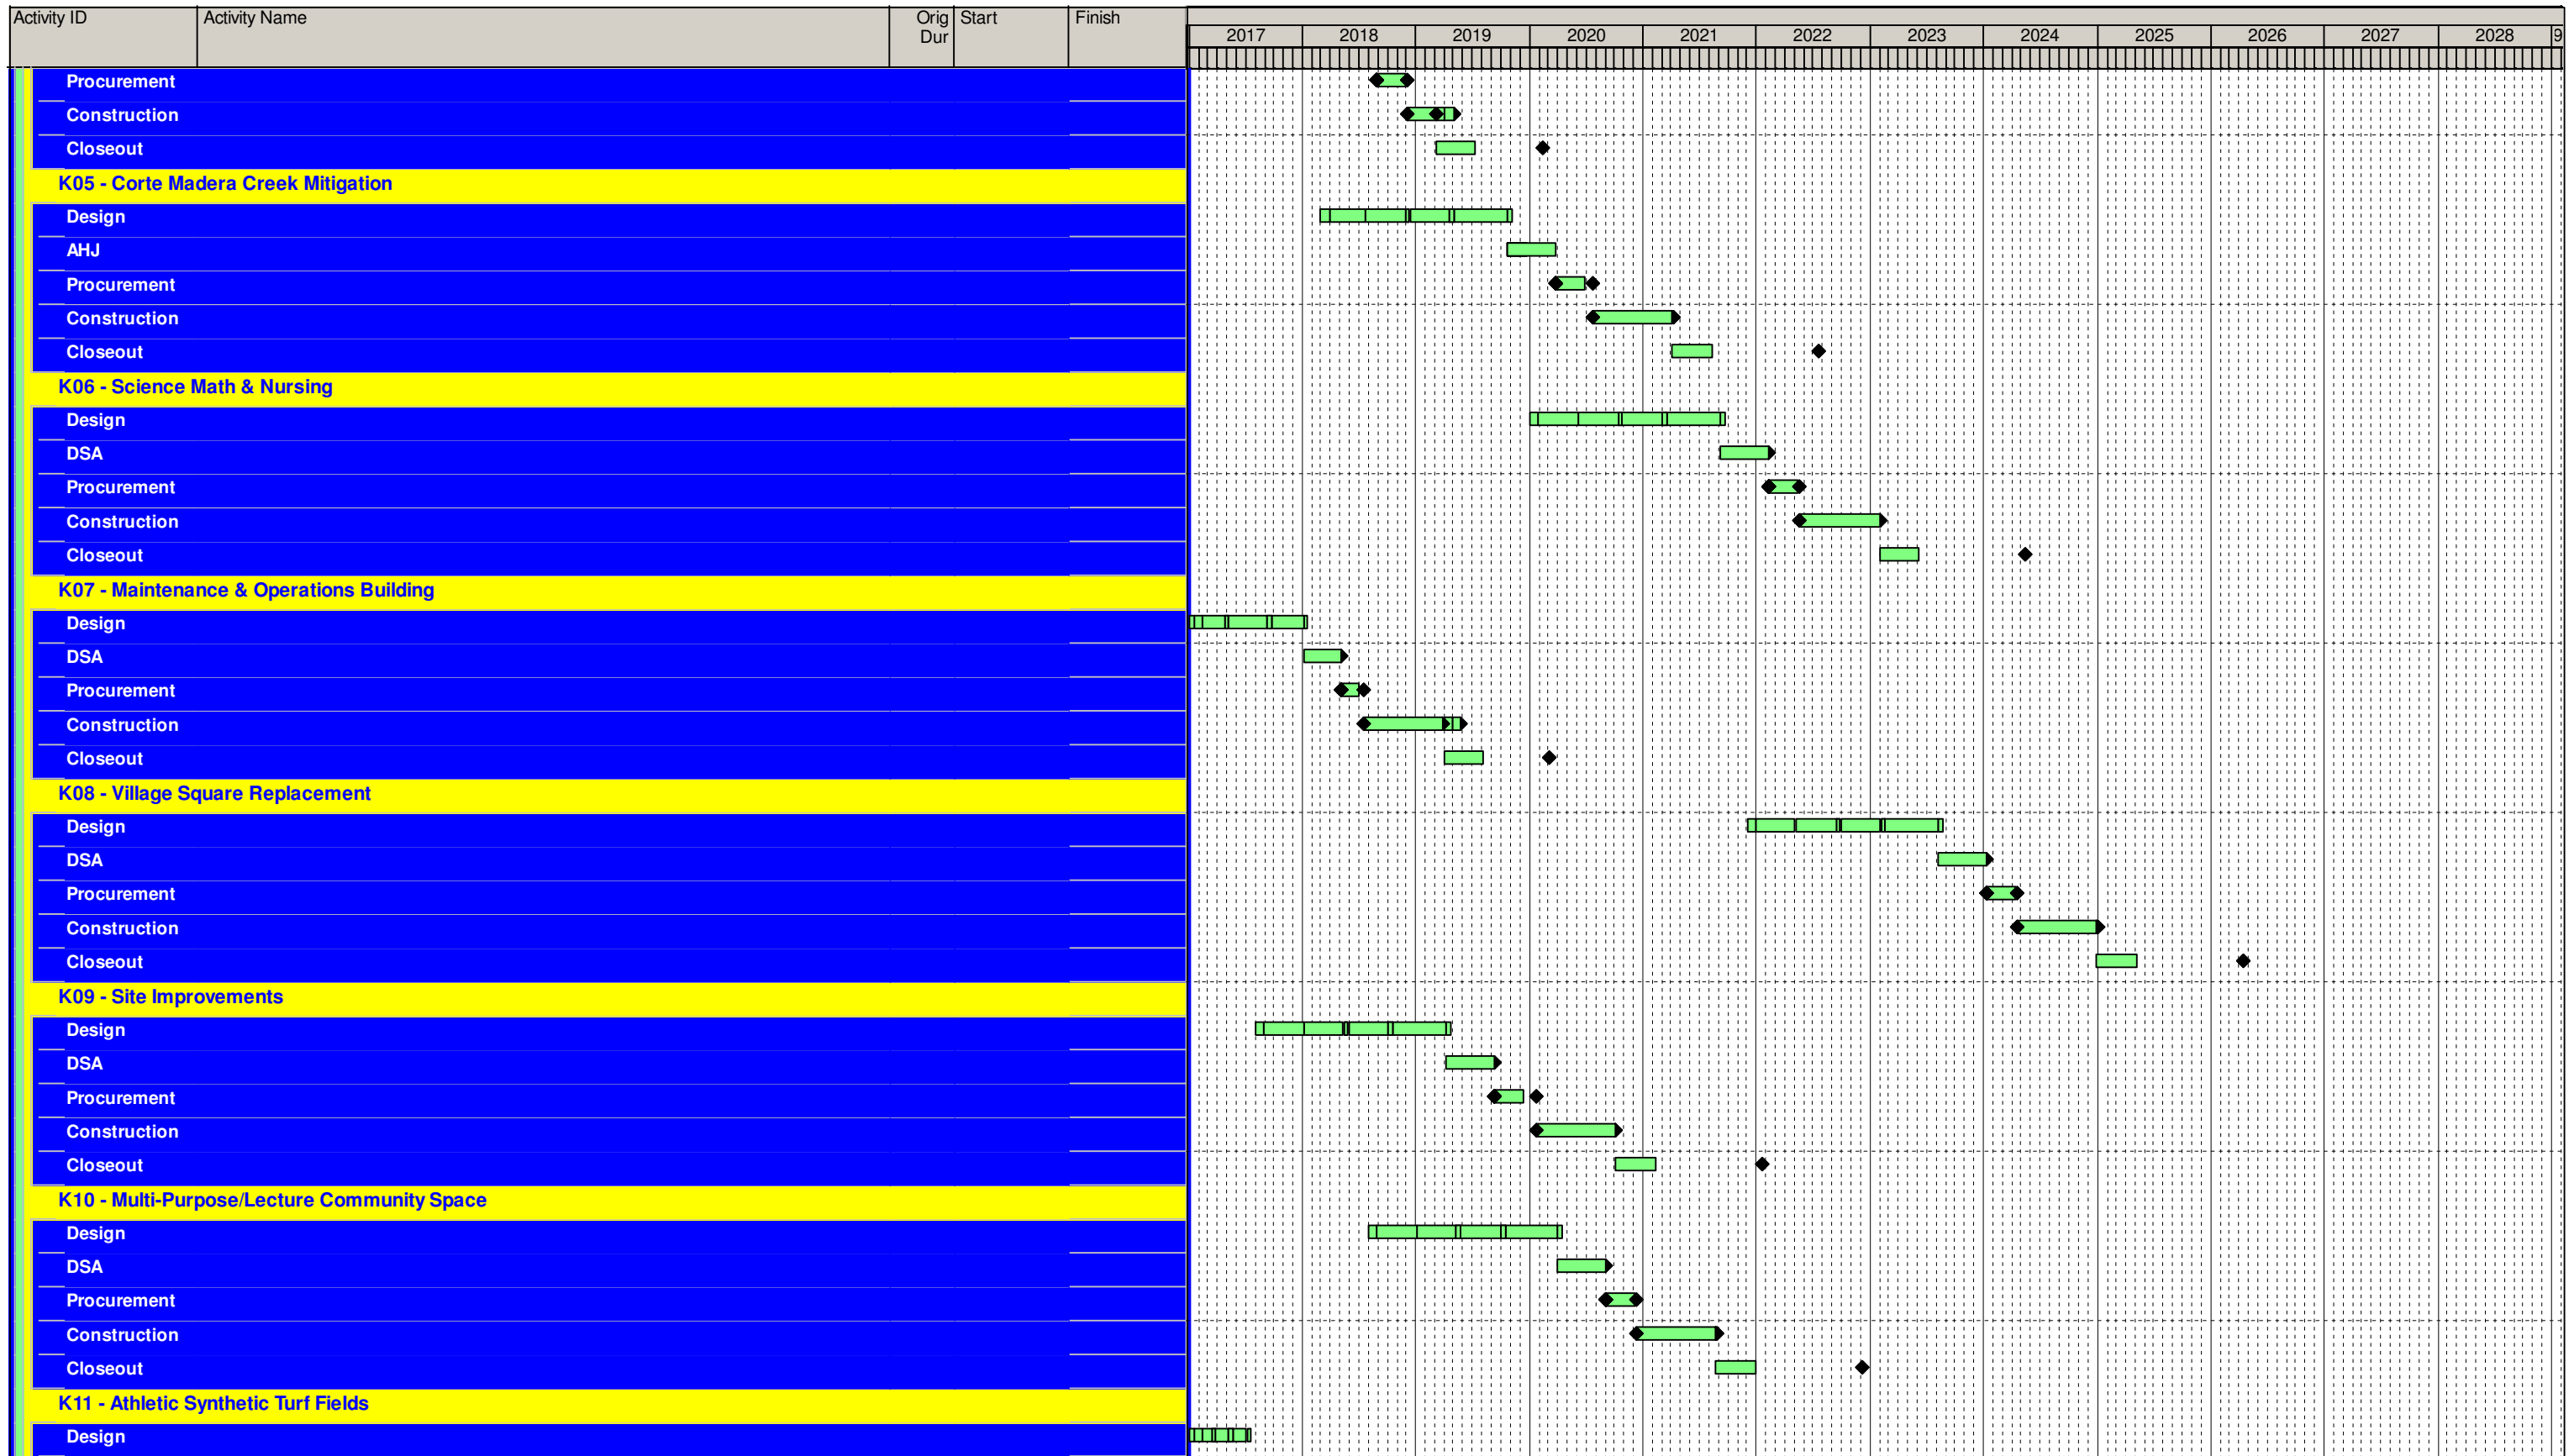


Finish Date: 01-Aug-28
 Data Date: 01-Jan-17
 Run Date: 11-Jul-17 11:05
 Page 3 of 5
 COM-001



College of Marin



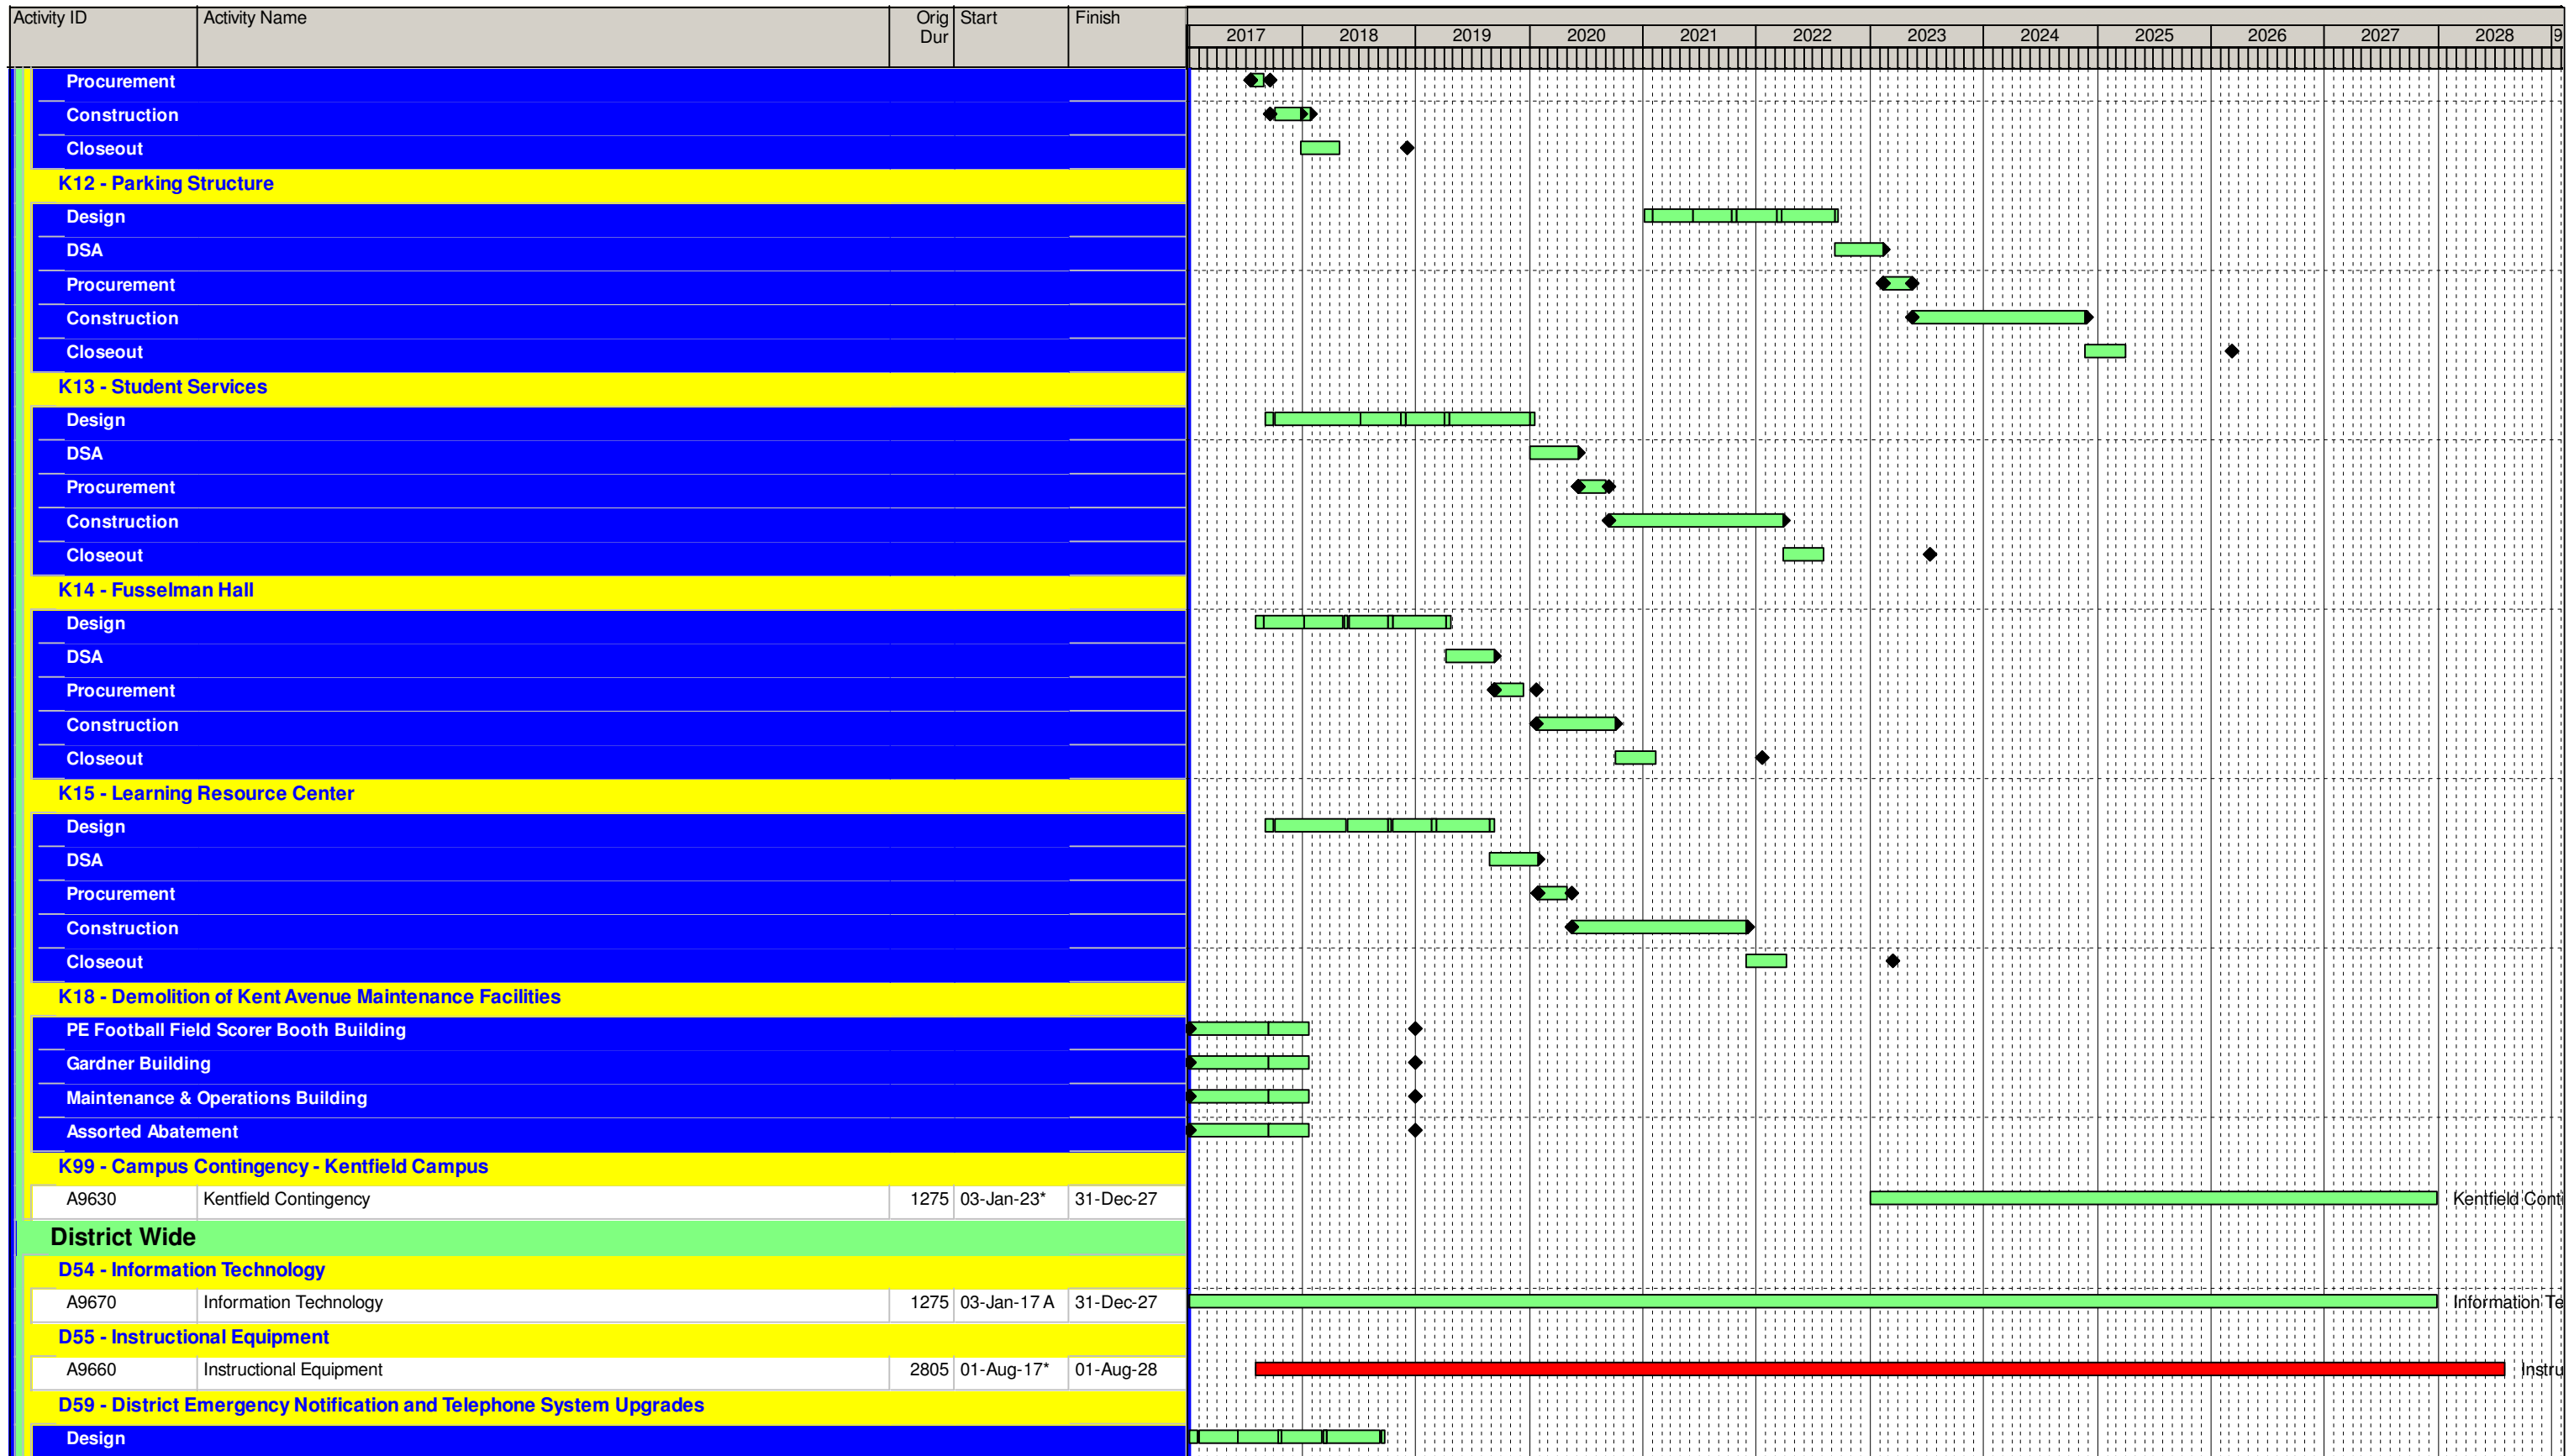

Finish Date: 01-Aug-28
 Data Date: 01-Jan-17
 Run Date: 11-Jul-17 11:05
 Page 4 of 5
 COM-001









	Remaining Level of Effort		Critical Milestones
	Actual Level of Effort		Milestone
	Actual Work		
	Remaining Work		
	Critical Remaining Work		
	Summary Milestones		

College of Marin



Activity ID	Activity Name	Orig Dur	Start	Finish	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	9
DSA																	
Procurement																	
Construction																	
Closeout																	
D98 - Program Management, District Staff																	
A9650	Program Management, District Staff	2613	02-Oct-17*	31-Dec-27													
D99 - District Wide/Program Contingency																	
A9640	Program Contingency	1275	03-Jan-23*	31-Dec-27													

Finish Date: 01-Aug-28
 Data Date: 01-Jan-17
 Run Date: 11-Jul-17 11:05
 Page 5 of 5
 COM-001

	Remaining Level of Effort		Critical Milestones
	Actual Level of Effort		Milestone
	Actual Work		
	Remaining Work		
	Critical Remaining Work		
	Summary Milestones		

College of Marin

